

[REDACTED]
TransGrid
200 Old Wallgrove Road
Wallgrove NSW 2766

27/01/2021

Dear [REDACTED]

**Powering Sydney's Future (SSI 8583)
Variation to Approved Construction Hours –
Sydenham Road and Old Canterbury Road trenching and conduit installation**

I refer to your request (SSI-8583-PA-45) submitted on 20 January 2021 for the Planning Secretary's approval of high risk out of hours works for the Powering Sydney's Future project (SSI 8583).

The Department notes that your previous request in relation to this package of high risk out of hours works for the Powering Sydney's Future project (SSI 8583-PA-41) was approved by the Planning Secretary on 14 January 2021.

The Planning Secretary's previous letter of approval, dated 14 January 2021, is subsequently superseded by this updated approval letter.

The Department has reviewed your revised requests to extend construction hours to carry out trenching, conduit installation and road restoration on Old Canterbury Road and sections of Hanks Street and Arlington Street, Hurlstone Park.

I note there are no revisions to the package of works for Sydenham, Road, Marrickville.

The Department accepts the requests to vary constructions hours subject to the following:

Sydenham Road, Marrickville package of works:

1. The works must be undertaken as detailed in the *Out of Hours Works Permit* (008 Rev 1) prepared by Taihan (SSI-8583-PA-41) and in accordance with the *Out of Hours Works Construction Noise and Vibration Impact Statement* (prepared by VMS Australia dated 3 September 2020), unless otherwise varied by the conditions below.
2. Work must not be undertaken outside the hours of work identified in Condition E4 of SSI 8583 (Approval), except for the works and hours detailed below:

- a) up to 34 shifts of night work on Sydenham Road, Marrickville around the intersection with Centennial Street, in the area delineated in Figure 1 of the *Out of Hours Works Permit* (008 Rev 1), between 20.00 on 22 January 2021 and 05.00 on 30 April 2021.

Old Canterbury Road and sections of Hanks Street and Arlington Street, Hurlstone Park package of works

1. The works must be undertaken as detailed in the *Out of Hours Works Permit* (009 Rev 03) prepared by Taihan (SSI-8583-PA-45) and in accordance with the *Out of Hours Works Construction Noise and Vibration Impact Statement* (prepared by VMS Australia dated 3 September 2020), unless otherwise varied by the conditions below.
2. Work must not be undertaken outside the hours of work identified in Condition E4 of the Approval, except for the works and hours detailed below:
 - a) Conduit installation: up to 14 days, including ten-night shifts (18:00–07:00 the following day) and two Saturday afternoon shifts (13:00–18:00), from 27 January 2021, on Old Canterbury Road and sections of Hanks Street and Arlington Street, Hurlstone Park, in the area delineated in Figure 1 of the *Out of Hours Works Permit* (009 Rev 03). Work will be carried out during day and night shifts, as per TMC approval. There will be a maximum of six consecutive day shifts and five night shifts per week.
 - b) Road restoration will be completed following TMC road occupancy approval. Work will take place over seven days, including five night shifts (18:00-07:00 following day) and one Saturday afternoon shift (13:00-18:00). Shift pattern will reflect the below. The end date of OOHW is 27 April 2021.

Applicable to both packages of out of hours works being Sydenham Road, Marrickville and Old Canterbury Road and sections of Hanks Street and Arlington Street, Hurlstone Park:

3. Written notice must be provided to surrounding residential occupiers and placed on site at least 48 hours before work occurs outside the normal construction hours identified in Condition E4. The written notice must:
 - I. identify what works are to occur outside normal construction hours;
 - II. nominate the timeframe the works are likely to occur;
 - III. be reissued 24 hours before any work occurs outside normal construction hours if the wet weather requires an alternative day from that notified; and
 - IV. provide a telephone contact number dedicated to the project during that will be operational throughout the extended construction hours.
4. A record of any complaints made regarding works undertaken during the extended construction hours must be provided to the Department's Compliance team within 24 hours of the complaint.
5. In the event that any complaint is received, appropriate mitigation measures are to be implemented, and the Department and the complainant are to be informed of the actions undertaken to address the complaint.
6. All noise management controls as described in Section 9 of the *Out of Hours Works Noise and Vibration Impact Statement* (prepared by VMS Australia dated 3 September 2020), are to be adopted and implemented for the duration of the works.

Yours sincerely

A handwritten signature in blue ink, consisting of several loops and a long horizontal stroke extending to the right.A black rectangular redaction box covering the signature area.

As nominee of the Planning Secretary

PSF OUT-OF-HOURS WORK PERMIT

(For works conducted under DPIE approval)

Permit No.	009		Application Date	21/12/2020
Revision No.	03		Revision Date	20/01/2021
Summary of Update (details of revision)	3	Application revised based on working 24/7. Additional respite included.		
Title of Works	Canterbury Road trenching and conduit installation			
Person Requesting OOHW	[REDACTED]			

1.0 - JUSTIFICATION	
Justification for OOHW	TMC have requested the works be completed 24/7 to minimise impact to road users.
DPIE Condition under which works are permitted	<i>Include additional details if required</i> The work is permitted under the following clause of DPIE Condition of Approval: E4 (c): Linear infrastructure – Works in classified road reserves and signalised intersections. E6 (c): works approved under an Out-of-Hours Work Protocol

2.0 – DESCRIPTION OF THE WORKS		
Details of Work ☒ Map attached at end of form (showing location / work extent / nearest sensitive receivers / landscape)	Location & Chainage	CH11,800 Hanks St to CH12,350 Arlington St, along Old Canterbury Rd.
	Description of works	Trenching, conduit installation and road restoration.
	Proposed dates + time (incl contingency)	Start: 27/01/2021 @ 18:00 Finish: 27/04/2021 @ 07:00* *Conduit installation works are scheduled to take place over 14 days, including 10 night shifts (18:00-07:00 following day) and two Saturday afternoon shifts (13:00-18:00), from 27/01/21. Work will be carried out during day and night shift, as per TMC road occupancy approval. There will be a maximum of six consecutive day shifts and five night shifts per week. Indicative shift pattern and respite shown below. Exact dates may vary due to unforeseen circumstances – contingency included in the date range above. Road restoration will be completed at a later date in approximately one week pending TMC road occupancy approval. Work will take place over 7 days, including 5 night shifts (18:00-07:00 following day) and one Saturday afternoon shift (13:00-18:00). Shift pattern will reflect the below. Exact dates not confirmed at this time – contingency included in the date range above.

2.0 – DESCRIPTION OF THE WORKS								
	Proposed Timings and activities	Indicative shift pattern – 6 day shifts and 5 night shifts per week during the proposed dates.						
		Monday – 17 hours 07:00-23:59	Tuesday – 24 hours 00:00-23:59	Wednesday – 24 hours 00:00-23:59	Thursday – 24 hours 00:00-23:59	Friday – 24 hours 00:00-23:59	Saturday – 18 hours 00:00-18:00	Sunday – 0 hours
		Respite - No works before 7am	Saw-cutting and concrete breaking completed 07:00-18:00	Saw-cutting and concrete breaking completed 07:00-18:00	Saw-cutting and concrete breaking completed 07:00-18:00	Saw-cutting and concrete breaking completed 07:00-18:00	Saw-cutting and concrete breaking completed 07:00-18:00	Respite - No work on Sunday.
		Saw-cutting and concrete breaking completed 07:00-18:00	Rock hammering will be completed during day shift where possible, but no later than 00:00.	Rock hammering will be completed during day shift where possible, but no later than 00:00.	Rock hammering will be completed during day shift where possible, but no later than 00:00.	Rock hammering will be completed during day shift where possible, but no later than 00:00.	Rock hammering will be completed during day shift.	
		Rock hammering will be completed during day shift where possible, but no later than 00:00.	Anytime: Excavation Conduit install TSB Road restorations (Plates if required)	Anytime: Excavation Conduit install TSB Road restorations (Plates if required)	Anytime: Excavation Conduit install TSB Road restorations (Plates if required)	Anytime: Excavation Conduit install TSB Road restorations (Plates if required)	Anytime: Excavation Conduit install TSB Road restorations (Plates if required)	
		Anytime: Excavation Conduit install TSB Road restorations (Plates if required)	Anytime: Excavation Conduit install TSB Road restorations (Plates if required)	Anytime: Excavation Conduit install TSB Road restorations (Plates if required)	Anytime: Excavation Conduit install TSB Road restorations (Plates if required)	Anytime: Excavation Conduit install TSB Road restorations (Plates if required)	Anytime: Excavation Conduit install TSB Road restorations (Plates if required)	
		Anytime: Excavation Conduit install TSB Road restorations (Plates if required)	Anytime: Excavation Conduit install TSB Road restorations (Plates if required)	Anytime: Excavation Conduit install TSB Road restorations (Plates if required)	Anytime: Excavation Conduit install TSB Road restorations (Plates if required)	Anytime: Excavation Conduit install TSB Road restorations (Plates if required)	Anytime: Excavation Conduit install TSB Road restorations (Plates if required)	
		Anytime: Excavation Conduit install TSB Road restorations (Plates if required)	Anytime: Excavation Conduit install TSB Road restorations (Plates if required)	Anytime: Excavation Conduit install TSB Road restorations (Plates if required)	Anytime: Excavation Conduit install TSB Road restorations (Plates if required)	Anytime: Excavation Conduit install TSB Road restorations (Plates if required)	Anytime: Excavation Conduit install TSB Road restorations (Plates if required)	
		Anytime: Excavation Conduit install TSB Road restorations (Plates if required)	Anytime: Excavation Conduit install TSB Road restorations (Plates if required)	Anytime: Excavation Conduit install TSB Road restorations (Plates if required)	Anytime: Excavation Conduit install TSB Road restorations (Plates if required)	Anytime: Excavation Conduit install TSB Road restorations (Plates if required)	Anytime: Excavation Conduit install TSB Road restorations (Plates if required)	
		Anytime: Excavation Conduit install TSB Road restorations (Plates if required)	Anytime: Excavation Conduit install TSB Road restorations (Plates if required)	Anytime: Excavation Conduit install TSB Road restorations (Plates if required)	Anytime: Excavation Conduit install TSB Road restorations (Plates if required)	Anytime: Excavation Conduit install TSB Road restorations (Plates if required)	Anytime: Excavation Conduit install TSB Road restorations (Plates if required)	
Details on any concurrent construction activities being undertaken OOWH adjacent / in close proximity to the proposed works?		N/A						
Names of Foremen supervising the work								
Subcontractor Details		Garde Services Durkin Locators						

3.0 – SENSITIVE RECEIVERS				
Distance to Nearest Sensitive Noise Receiver	Sensitive Receiver	Distance	Sensitive Receiver	Distance
	☐ Place of Worship		☐ Educational Institution (inc. Child Care Centres)	
	☐ N+V Sensitive Business and critical working area (eg. theatre, health services)		☒ Nearest Residential Receiver	10m
	☐ Not applicable (no sensitive receivers impacted)			
	<i>Where one of the above is checked, noise generating works must not be timetabled within sensitive periods, unless otherwise agreed with the affected receiver. This must be determined through ongoing consultation with the community in accordance with the Community Consultation Strategy.</i>			
	Has the sensitive receiver been consulted on these works and proposed respite options? (refer to CoA E9). List outcomes of consultation below ☒ Yes ☐ No			
	Comments Two rounds of community consultation have been conducted via notification distribution and doorknocking to inform this permit application. See attached. Further community notifications will be distributed 7 days ahead of works commencing. Individual briefings will be conducted for those requesting them or deemed highly sensitive by the Community Relations Manager. Project specific respite offers, for example movie tickets, may be offered to members of the community subjected to lengthy periods of noise or vibration. This will be determined on a case-by-case basis.			

4.0 – PLANT & EQUIPMENT	
Plant and equipment to be used: List all plant and noise generating equipment to be used during the work activities (eg. hand tools, generators, crane etc)	13t Excavator & hammer 5t excavator Truck & dogs 8-wheeler bogie Concrete agitators Compaction equipment (Whackers, plate compactors) Smooth drum roller Light vehicles
Are alternative, quieter / less vibration intensive equipment options feasible for the activity? If yes, why are these not being used?	☐ Yes ☒ No

5.0 – TRAFFIC MANAGEMENT	
Will the work require traffic control?	☒ Yes ☐ No

5.0 – TRAFFIC MANAGEMENT

Describe the location and nature of proposed disruption to traffic.	During trenching works, traffic will be maintained but diverted around the work site on Old Canterbury Road. Traffic on side streets will be maintained via diversion.
List any ROLs for the works	ROL1551950

6.0 – LIGHTING

What lighting is to be provided for night work?	Daymakers Balloon lights
Will lighting be positioned to minimise light spill to nearby receivers?(Refer AS4282-1997 and AS/NZ 1158).	☒ Yes ☐ No

7.0 – NOISE & VIBRATION ASSESSMENT

Reference: NMC Noise Objective Noise Management Level (NML) Sleep Disturbance Level (night only) Predicted L_{max}/L_{A1}	NCA:	05						
	Type of OOHW:	Trenching and conduit installation						
	NML:	45						
	SDL:	65						
	Predicted:	85						
Acoustic Assessment to determine if works are above RBL +5dB(A) at closest receiver	☐  Below NML ☐  <5dB(A) above NML – construction noise noticeable ☐  5 to 15dB(A) above NML – construction noise clearly audible ☐  >15 to 25dB(A) above NML – construction noise moderately intrusive ☒  >25dB(A) above NML – construction noise highly intrusive							
What measures are being taken to reduce noise impacts	☐ No added measures ☒ Restrictive tools (<i>list</i>) – no greater than 13tonne excavator. Reverse quackers on trucks. ☒ Balloon lights ☒ Noise attenuation curtains ☒ High noise impact respite ☒ Other (<i>list</i>) – Road plates to be secured to minimise noise due to passing traffic.							
Noise monitoring required?	☒ Yes – Compliance monitoring to be carried out within the first two shifts ☐ No Nominated Verification monitoring location: <table border="1" style="width: 100%;"> <tr> <td>Worksite</td> <td>NCA</td> <td>Nominated receiver</td> </tr> </table>					Worksite	NCA	Nominated receiver
Worksite	NCA	Nominated receiver						

7.0 – NOISE & VIBRATION ASSESSMENT									
	Old Canterbury Road	NCA5	341 Old Canterbury Road (perimeter)						
Are vibration impacts above Human Comfort levels expected?	☒ Yes ☐ No Refer to OOH CNVIS Table 5		If yes, state number of properties expected to be impacted? No. of properties: Barely noticeable – 07 Noticeable - 48						
Is vibration monitoring required? Refer to CNVMP/Monitoring Programme	☒ Yes – Compliance monitoring to be carried out within the first two shifts. ☐ No Nominated Verification monitoring location: <table border="1" style="width: 100%; margin-top: 5px;"> <thead> <tr> <th>Worksite</th> <th>NCA</th> <th>Nominated receiver</th> </tr> </thead> <tbody> <tr> <td>Sydenham Road</td> <td>NCA5</td> <td>341 Old Canterbury Road (perimeter)</td> </tr> </tbody> </table>			Worksite	NCA	Nominated receiver	Sydenham Road	NCA5	341 Old Canterbury Road (perimeter)
Worksite	NCA	Nominated receiver							
Sydenham Road	NCA5	341 Old Canterbury Road (perimeter)							
Community notification required?	Yes. Community notifications will be undertaken as per the approved Community Communication Strategy (CCS), including; Consultation on preferred respite option Letters notifying of work activities to be delivered 7 days before. A door knock will be done for the sensitive receivers immediately adjacent to the works as per CNVMP. Individual briefings may be held where requested by the Community or where deemed appropriate by the Community Team Manager.								
Evidence of consultation and results	<u>Consultation documentation submitted with this application.</u> <u>Summary of Results:</u> 136 receivers consulted on preferred respite via notification. 48 consulted via doorknock. 33 responses received. Of those expressing a preference, 53% favoured option 2, six consecutive nights per week, 40% favoured option 1, four consecutive nights and 7% favoured baseline OOH - no more than two consecutive nights per week.								

8.0 – OOHW RISK LEVEL ASSESSMENT

Insert snip from Risk Level calculation sheet and attach worksheet separately

Low Risk (1-6)
Moderate (7-9)
High (10-12)

Low and Moderate risk work may be approved by the ESM.

High risk work must be approved by the Planning Secretary.


Overall Risk Assessment	Sum of Risk Factor Scores	Approval Path
Low 1 Risk Activity	1 - 6	Environment and Sustainability Manager
Moderate 2 Risk Activity	7 - 9	Environment and Sustainability Manager
High Risk Activity	10 - 12	Planning Secretary

Your total Risk score is:


12

Risk level calculator worksheet attached with application.

Work to be approved by Planning Secretary as per CoA E8(e).

9.0 AUTHORISATION/SITE ACCEPTANCE					
9.1 Environment & Sustainability Manager (Approval)					
Approval Authority for works with Low or Medium Risk level on OOHW Risk Table as per section 8.0 I confirm these works have been appropriately assessed under the OOHW Protocol as per CoA E8 and E9. The specified mitigation and management measures shall be implemented including: - No more than six consecutive days and five consecutive night shifts per week - Concrete breaking or saw-cutting to occur between 07:00 - 18:00. - Rock breaking may occur between 07:00-00:00. - Noise and vibration verification monitoring within the first two shifts. - Installation of noise barriers around high impact works. - Respite 1hr for every 3hr of high impact noise during day hours. - Respite 1hr for every 1hr of high impact noise during night hours. - Selection of appropriate plant and equipment. - Individual community briefings ahead of works commencing, and during works, as required. - Project specific respite offers may be made for residents impacted by lengthy periods of works. To be determined on a case-by-case basis.					
Name		Signature		Date	19/01/2021
9.2 Planning Secretary (Approval)					
REQUIRED					
Name		Signature		Date	
9.3 Construction Supervisor/Project Manager (Site Acceptance)					
I confirm the following: - OOH permit will be kept on site where work is occurring - Respite and mitigation measures will be implemented - Any changes to works which may affect this approval shall be communicated to the Environment and Community Manager					
Name		Signature		Date	20/01/2021

Attachment – Map of Works Location

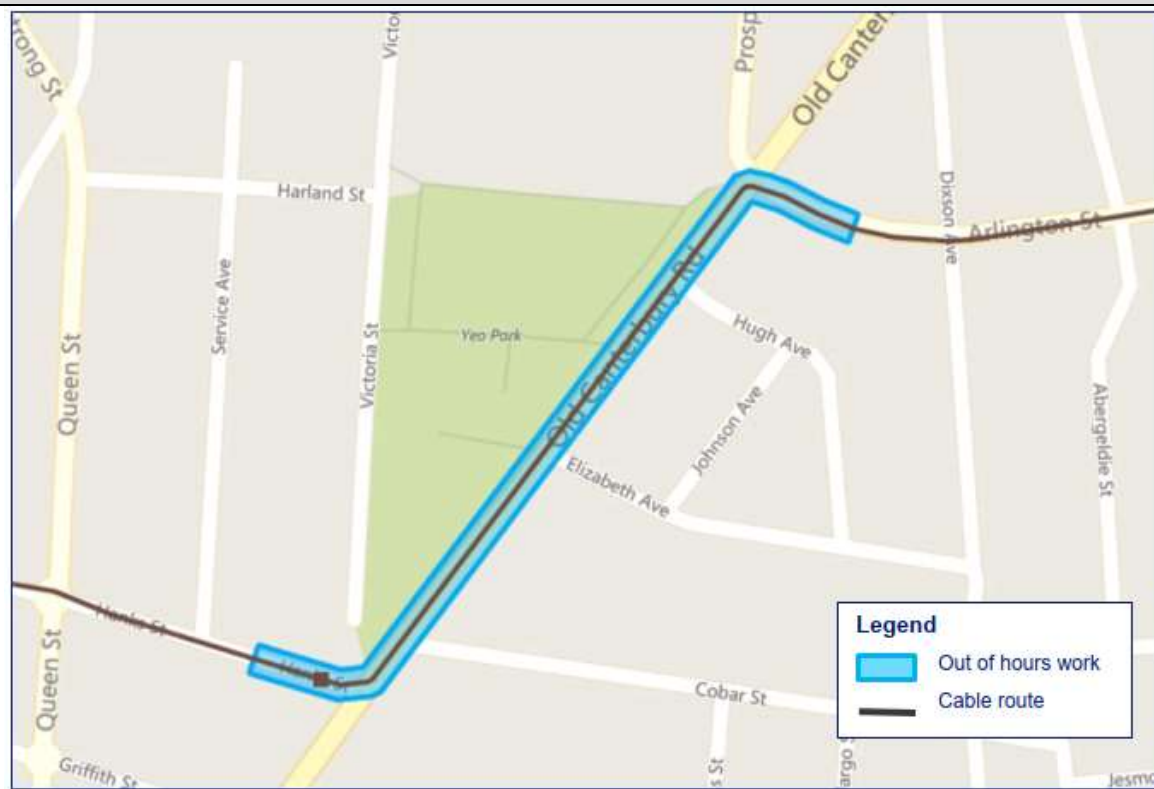**Figure 1:** Map of works location

Attachment – Map of Works Location

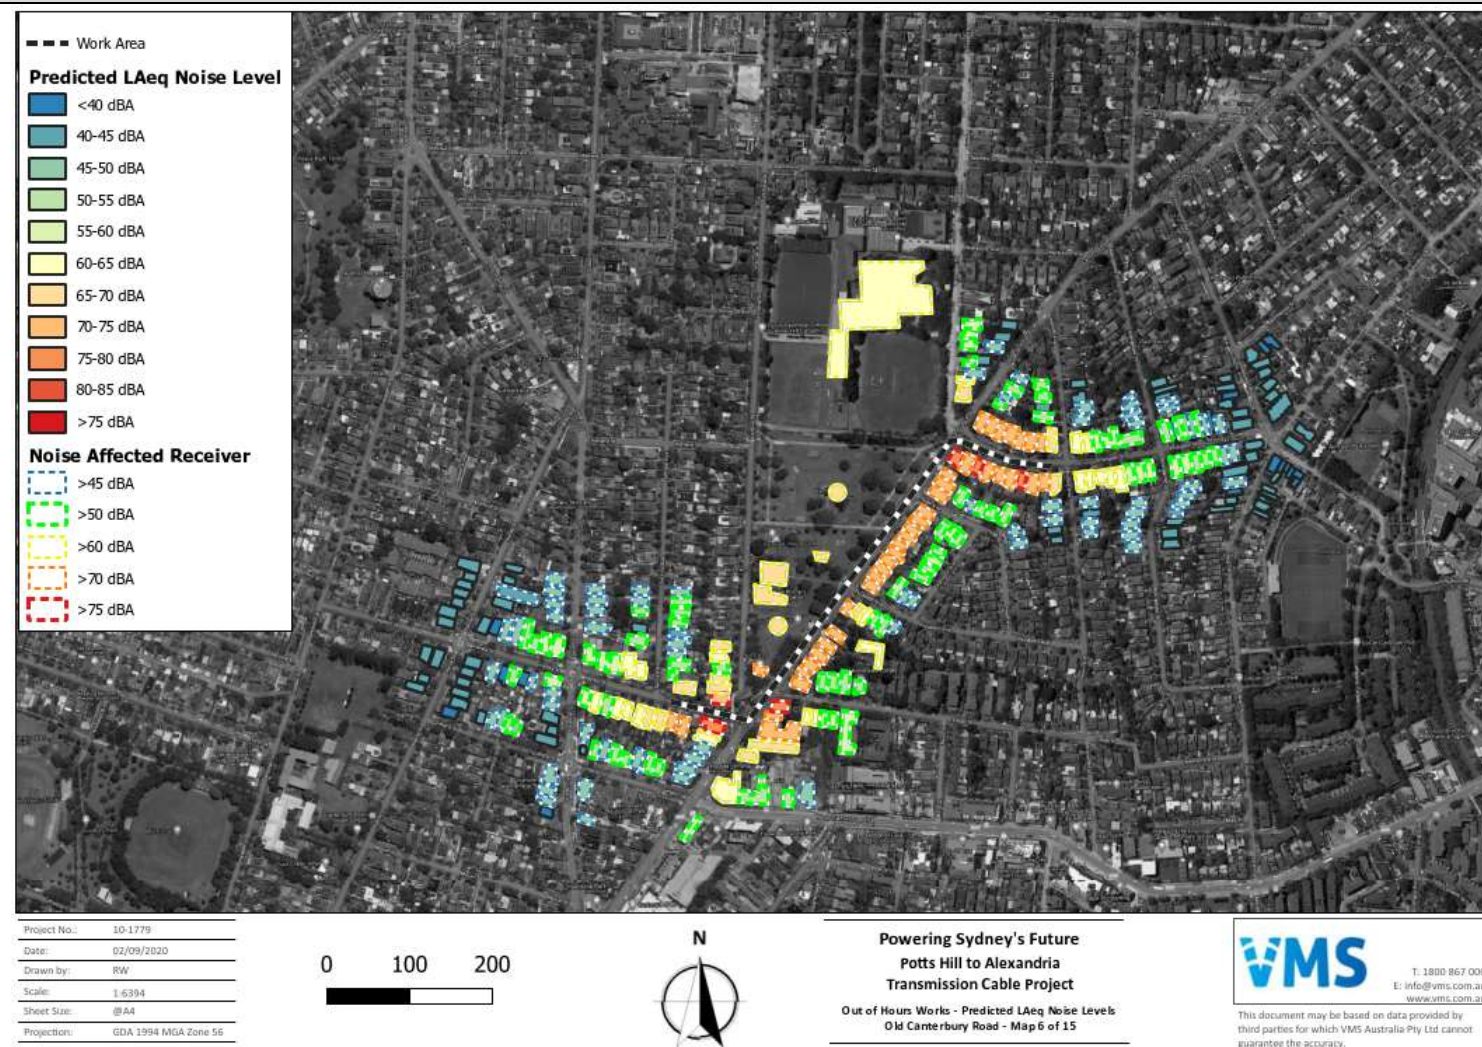


Figure 2: Map of potentially noise impacted receivers.

Attachment – Map of Works Location

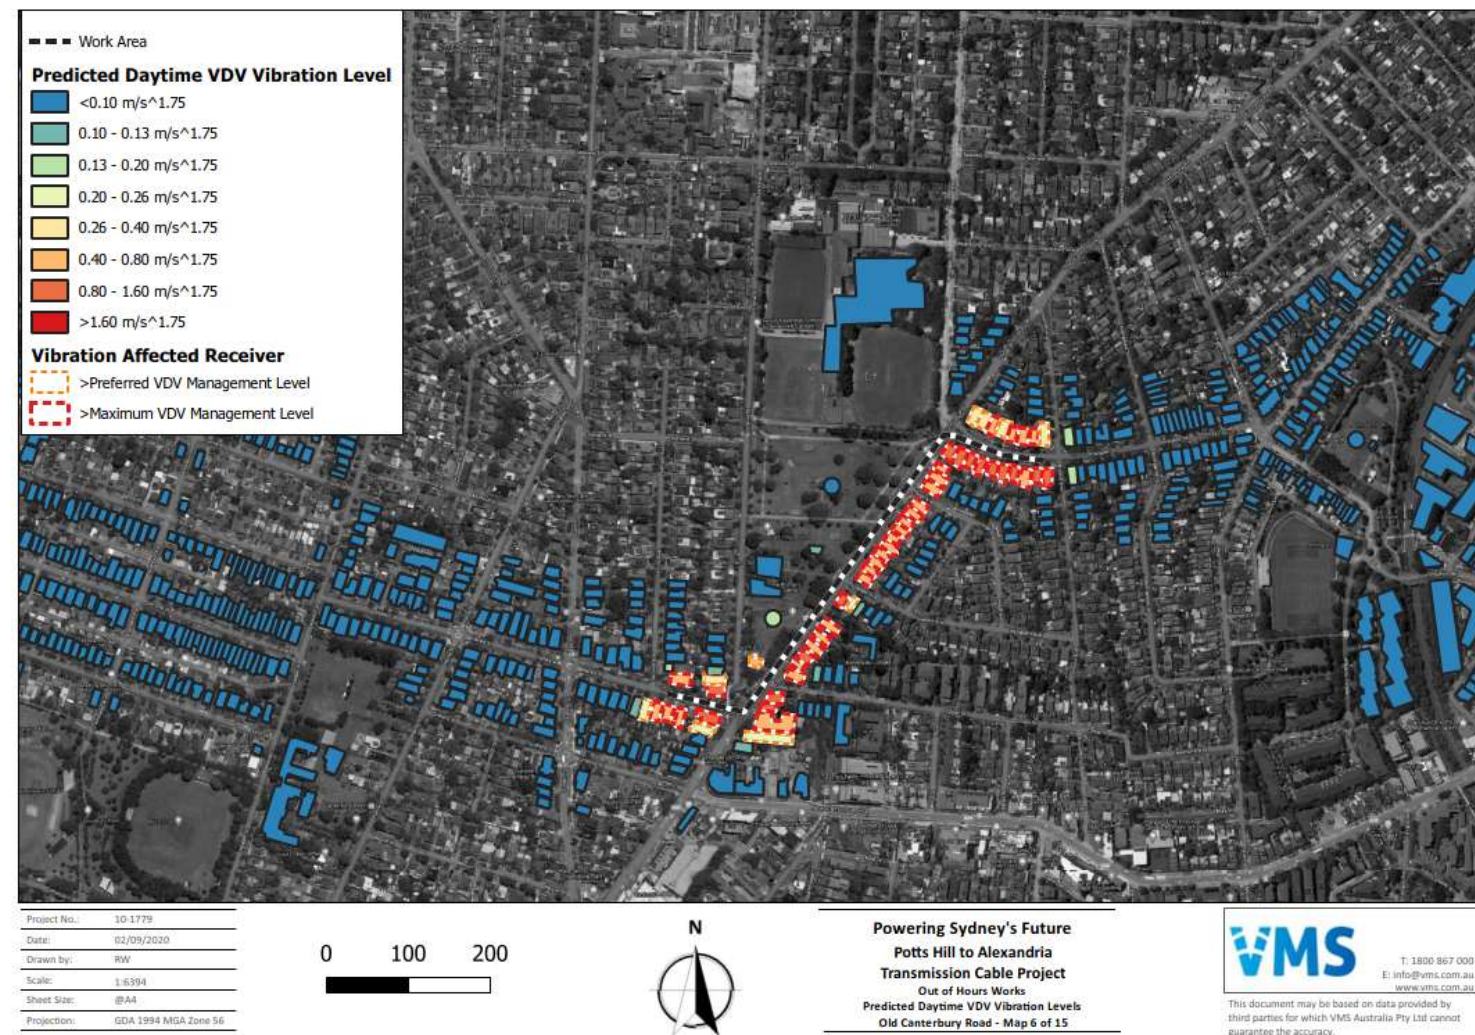


Figure 3: Map of potentially vibration impacted receivers.

Out of Hours Work

Activity Works	Activity / Impact	Time
Linear Infrastructure - Site preparation, trenching, excavation, joint bays, restoration of road services, other ☐	Delivery and Police ☐	Monday - Friday 7am - 6pm ☐
Substation Upgrade Works ☐	Emergency ☐	Monday - Friday 6pm - 7am ☒
Linear Infrastructure - Works in Classified Road Reserves and Signalised intersections, cable pulling and jointing ☒	Approved under Existing OOHW protocol ☐	Saturday 8am - 1pm ☐
Special crossings - Cable bridges and underboring ☐	> 75dBA COA E5 ☒	Saturday 1pm - 8am ☐
Construction Laydown Area ☐	>RBL + 5dBA ☐	Sundays and Public Holidays ☐
	<=45 NML ☐	
	> 45 NML ☐	
	Vibration perceptible inside Residence ☐	

OOHW Protocol is Triggered!!!

Receiver type	Day OOHW 7am - 6pm	Evening OOHW 6pm - 10pm	Night OOHW 10pm - 7am	Notes
Childcare	☐ Low (1)	☐ Low (1)	☐ Low (1)	Not Operating during OOH
Commercial	☐ Low (1)	☐ Low (1)	☐ Low (1)	Sensitivity of Premises to be confirmed through consultation
Industrial	☐ Low (1)	☐ Low (1)	☐ Low (1)	Sensitivity of Premises to be confirmed through consultation
Educational	☐ Low (1)	☐ Low (1)	☐ Low (1)	Not operating during OOH
Hotel	☐ Low (1)	☐ Low (1)	☐ Mod (2)	Sensitivity of Premises to be confirmed through consultation
Medical	☐ Low (1)	☐ Low (1)	☐ Low (1)	Sensitivity of Premises to be confirmed through consultation
Place of Worship	☐ Mod (2)	☐ Mod (2)	☐ Low (1)	Sensitivity of Premises to be confirmed through consultation
Recording Studio	☐ Mod (2)	☐ Mod (2)	☐ Low (1)	Sensitive periods during operational periods as agreed with facility through consultation
Recreation (active)	☐ Low (1)	☐ Low (1)	☐ Low (1)	Sensitive periods during normal periods of use and review of special events calendar

Recreation (Passive)	☐ Mod (2)	☐ Low (1)	☐ Low (1)	Sensitive periods during normal periods of use and review of special events calendar
Residential	☐ Low (1)	☐ Mod (2)	☒ High (3)	Risk subject to complaints management. Respite periods to be consulted for Highly Noise Intensive Works
Restaurant (Outdoor Dining)	☐ Mod (2)	☐ Mod (2)	☐ Mod (2)	Sensitivity of premises to be confirmed through consultation

Exceedance of NML	Day OOHW 7am - 6pm	Evening OOHW 6pm - 10pm	Nicht OOHW 10pm - 7am	Qualitative Description
<5dB	☐ Low (1)	☐ Low (1)	☐ Low (1)	Barely noticeable exceedance of the NML
5 - 15 dB	☐ Low (1)	☐ Low (1)	☐ Mod (2)	Noticeably audible exceedance of the NML
15 - 25 dB	☐ Low (1)	☐ Mod (2)	☐ Mod (2)	Clearly audible exceedance of the NML
>25 dB	☐ Mod (2)	☐ High (3)	☐ High (3)	Intrusive exceedance of the NML
>75 dBA	☐ Mod (2)	☐ High (3)	☒ High (3)	Highly affected receivers

Vibration Assessment in Residential Areas (click here if Not Applicable) ☐	Day OOHW 7am - 6pm	Evening OOHW 6pm - 10pm	Nicht OOHW 10pm - 7am	Qualitative Description
Less than Preferred	☐ Low (1)	☐ Low (1)	☐ Low (1)	No noticeable floor vibration
Greater than Preferred, but Less than Maximum	☐ Low (1)	☐ Mod (2)	☒ Mod (2)	Barely noticeable floor vibration
Greater than Maximum	☐ Low (1)	☐ Mod (2)	☐ High (3)	Noticeable floor vibration

Duration	Day OOHW 7am - 6pm	Evening OOHW 6pm - 10pm	Nicht OOHW 10pm - 7am	Qualitative Description
1 day	☐ Low (1)	☐ Low (1)	☐ Low (1)	Generally Tolerable
2 days	☐ Low (1)	☐ Mod (2)	☐ Mod (2)	Marginal Annoyance
3 days	☐ Low (1)	☐ Mod (2)	☐ High (3)	Moderate Annoyance
More than 3 days	☐ Low (1)	☐ High (3)	☒ High (3)	Highly Disturbing

Get Risk Score

Overall Risk Assessment	Sum of Risk Factor Scores	Approval Path
Low 1 Risk Activity	1 - 6	Environment and Sustainability Manager
Moderate 2 Risk Activity	7 - 9	Environment and Sustainability Manager
High Risk Activity	10 - 12	Planning Secretary

Your total Risk score is:

12

Powering Sydney's Future

POTTS HILL TO ALEXANDRIA TRANSMISSION CABLE PROJECT COMMUNITY CONSULTATION

Out-of-hours work at Old Canterbury Road, Dulwich Hill

TransGrid is installing a new underground electricity cable from Potts Hill to Alexandria. The Powering Sydney's Future project will help ensure a safe, reliable and affordable electricity supply for Sydney's CBD and surrounding areas. You can view a map of the cable route at www.transgrid.com.au/psf.

At **Old Canterbury Road, Dulwich Hill** (intersections with Hanks Street and Arlington Street) we will need to work outside standard construction hours due to high daytime traffic volumes. These works will generate noise. The loudest activities will be saw cutting and hammering, followed by trenching, road restoration and tree trimming.

Out-of-hours work in this location is due to start from **mid-January 2021** and will require around **45 shifts**.

Propose work hours

Depending on the approval from the relevant road authorities, this out-of-hours work will either take place over a weekend shutdown from 6.00pm Friday through 6.00am Monday or would be carried out between 7.00am to 7.00pm from Monday to Sunday. We will keep you updated on the final work hours at least seven days in advance.

How will the work affect you?

- > **There will be around 45 shifts** of out-of-hours construction work in total.
- > Highly noise intensive work will be done for three hours at a time, followed by one hour of respite.
- > We aim to do high impact noise activities before midnight wherever possible.
- > High impact noise typically occurs at the start and end of shifts, as we open up road pavement and then repair it.
- > Access to properties will be maintained at all times, unless we make alternative arrangements with you in advance.

Tell us your views

We would like your views on two different ways this work could be done:

- Option 1 - Four consecutive nights per week over 11-12 weeks, or
- Option 2 - Six consecutive nights per week over 7-8 weeks.

Please refer to the attached noise chart for typical noise levels from this type of work.

You are welcome to let the Powering Sydney's Future project team know which option you prefer by contacting us on **1800 955 588** or at psf@transgrid.com.au before **Monday, 14 December 2020**.

Please write **Canterbury Road** in the subject line of your email to identify the major road.



Connect with us


Community Information Line: **1800 955 588**

Email: psf@transgrid.com.au

Web: www.transgrid.com.au/psf



Out-of-hours work map

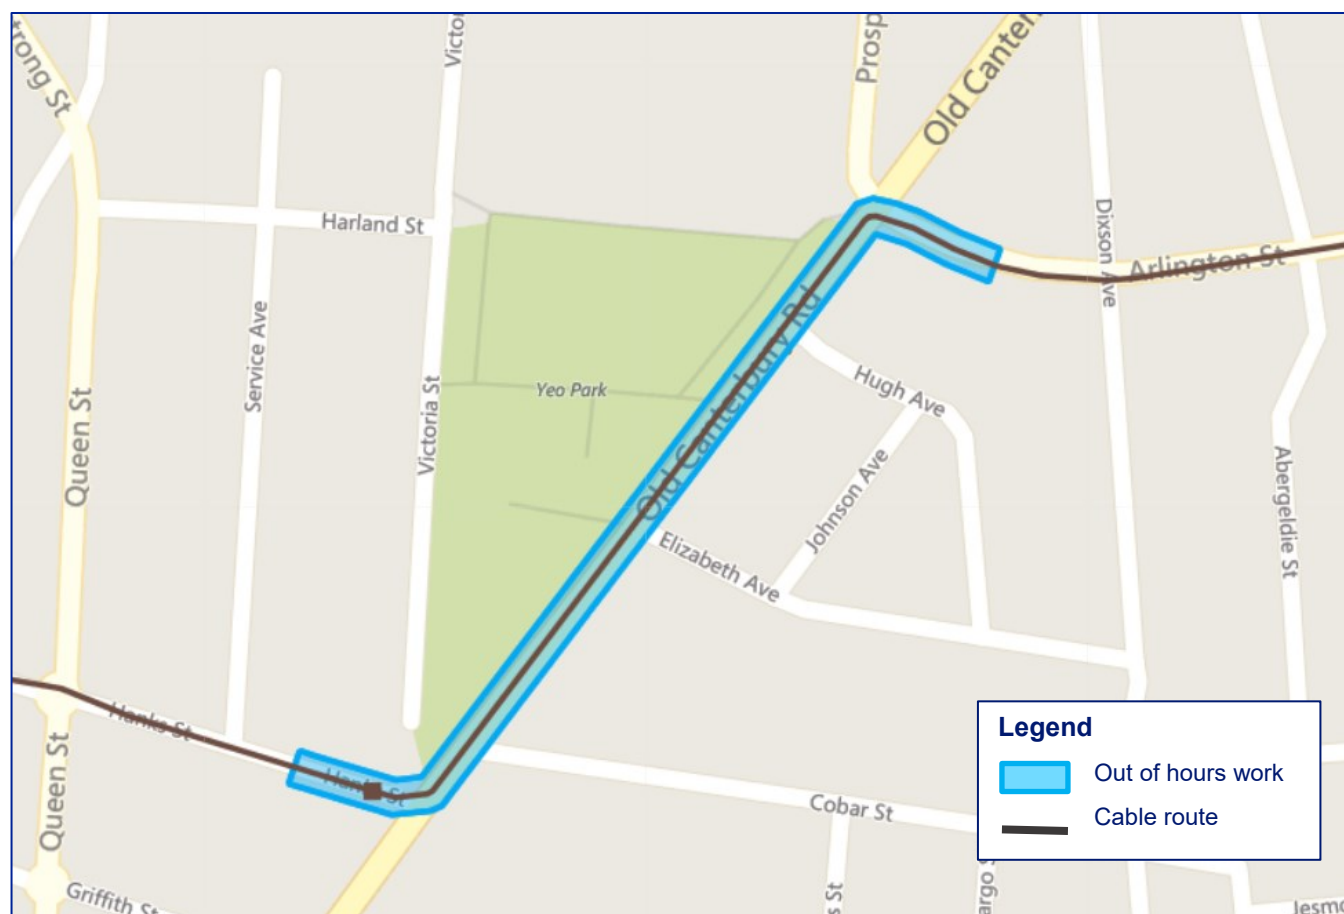

Noisy activities	Tools and equipment	Approximately 45 shifts over the period below			
		January	February	March	April
Saw cutting and hammering, trenching, road restoration and tree trimming	Powered saw, excavator hammer and bucket, hand operated compactor and small roller, chainsaws	✓	✓	✓	✓

COVID-19 Safety protocols

The health and safety of our people, customers and the community and ensuring a reliable supply of electricity to NSW and the ACT are our highest priorities during the COVID-19 crisis.

TransGrid and our contractors, as a minimum, adhere to the recommendations of SafeWork NSW along with the advice of other state and federal authorities to effectively manage the risk of COVID-19 to workers and others in the work environment. This involves maintaining effective controls including social distancing, stringent hygiene and specific access protocols at our work sites.



For an interpreter please call **131 450** and ask them to call TransGrid on **1800 955 588**. The interpreter will then assist you with translation.

**Connect
with us**


Please visit our website: www.transgrid.com.au/psf or contact the Powering Sydney's Future project team: Community Information Line: **1800 955 588** Email: psf@transgrid.com.au

Noise level comparisons



People’s perceptions of noise is strongly influenced by their environment.
A noise level that is perceived as loud in one situation may appear quiet in another.


dBa levels and subjective evaluation

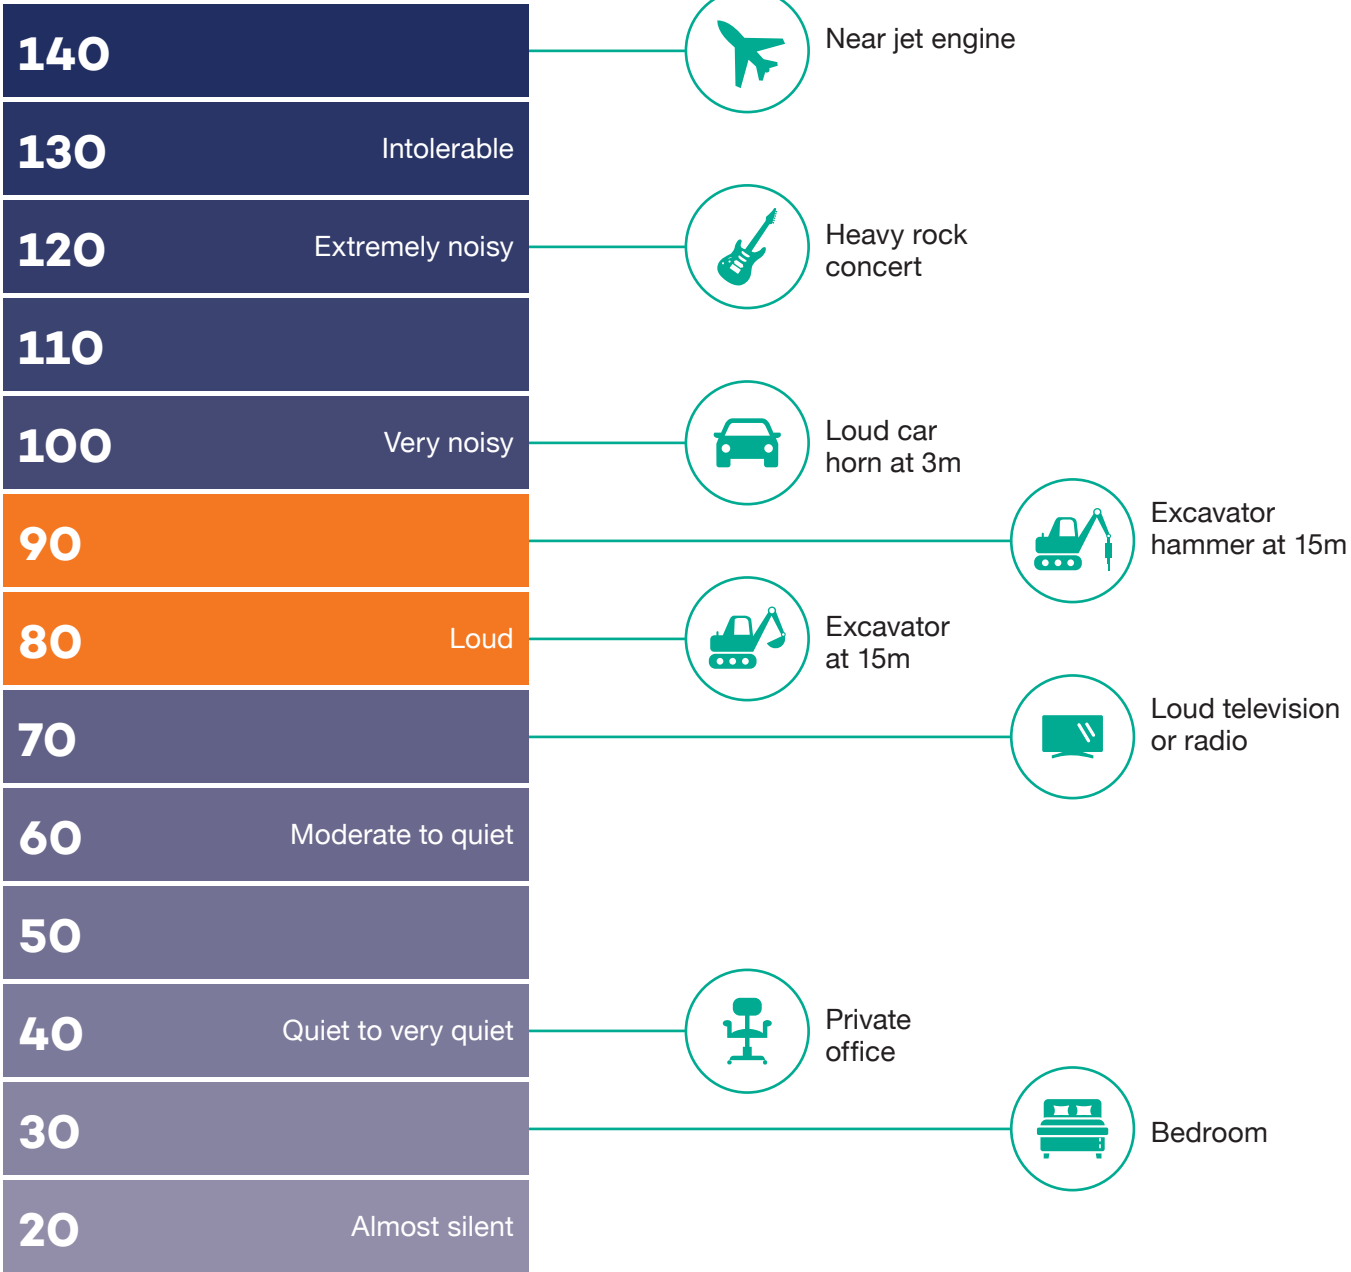

PSF-OOHW-009 Respite Consultation Report

Report	OOH Consultation for works at Old Canterbury Road	
Objective:	Obtain feedback about noise intensive works on Old Canterbury Road (intersections Arlington street and Hanks street) outside standard construction hours, 45 shifts.	
ITEM	#	%
Total of properties around 55DBA works	136	100%
Properties notified about the works and with OOH Consultation	136	100%
Properties with feedback after the notification	2	1.5%
Additional Activities.		
Properties contacted via doorknock to obtain the feedback around the 75 DBA or sensitive receivers.	48	-
Total of properties with feedback after the doorknock	33	68.75%
Total of properties without feedback	15	31.25%
Results		
Total of feedbacks	33	100%
Option 1: The work will be done over four consecutive night shifts, with three respite nights. – This option means we may be working near your property for over 11-12 weeks.	12	36.4% (40% of those expressing a preference)
Option 2: The work will be done over 6 consecutive night shifts, with one respite night – This option may allow completion of the work in around 7-8 weeks.	16	48.5% (53% of those expressing a preference)
The resident has informed the project team that they do not have a preference regarding night work plans.	3	9.1%
The resident preferred baseline of three nights per week.	2	6%

MAP OF THE AREA.

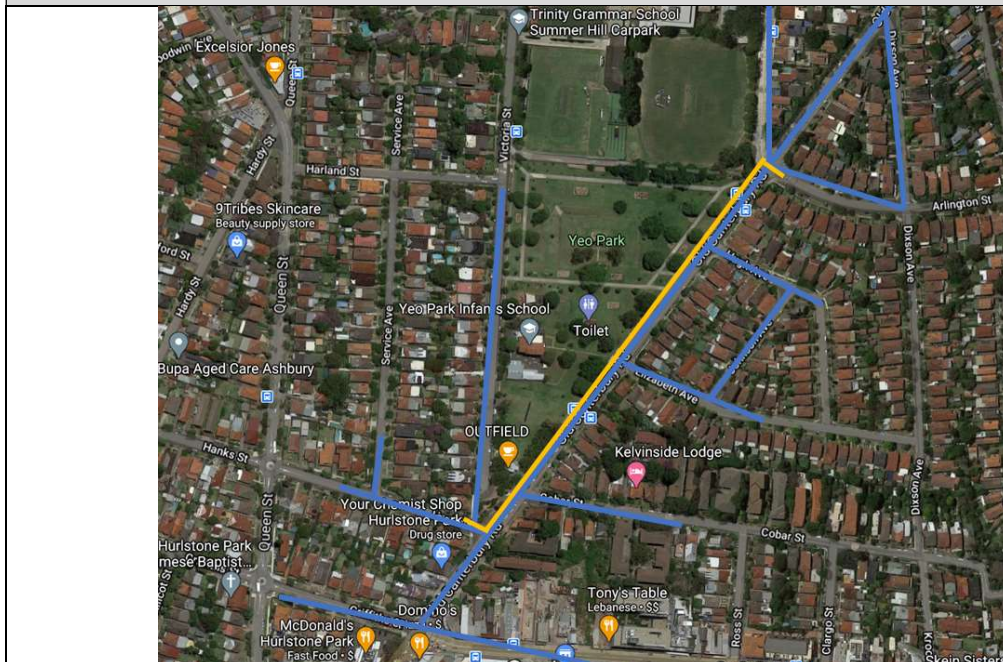

[illegible]

[illegible]

[illegible]

[illegible]

[illegible]
